Exoplanet Exploration Program Level 1 Schedule
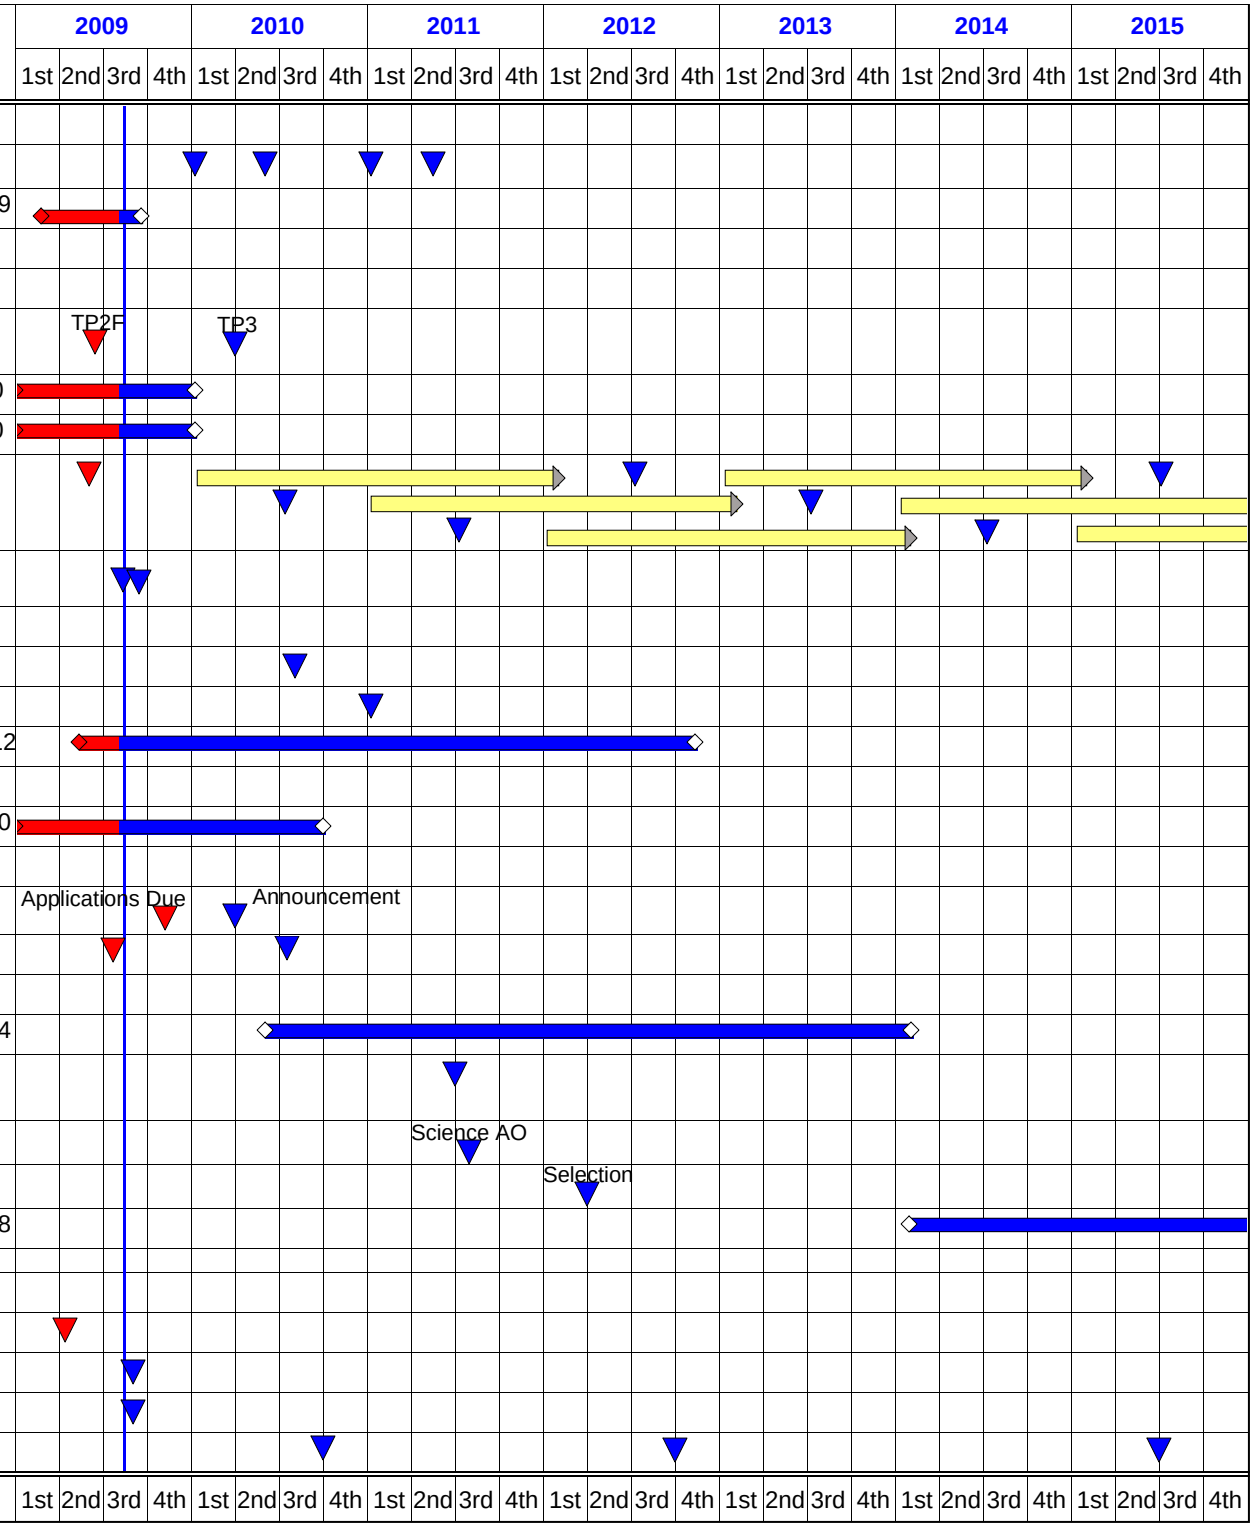
	Activity Name	Start Date	Finish Date
1	**Program Planning**		
2	ExoPAG Meetings	1/8/10 6/1/10	
3	Concept/Technology Assmt	2/24/09	9/16/09
4	**Program Elements**		
5	**Exoplanet Technology**		
6	Technology Plan	6/16/09 4/1/10	
7	Legacy Tasks	1/1/09	1/8/10
8	ASMCS Support	1/1/09	1/8/10
9	Technology NRA	6/1/09 7/12/10 7/11/11 7/9/12	
10	**Keck Interferometer**	8/10/09 9/16/09	
11	**LBTI**		
12	AO Secondary #2	8/2/10	
13	Shared Risk Science Start	1/10/11	
14	**Kepler Science Operations**	5/13/09	11/12/12
15	**SIM-Lite**		
16	SIM-Lite Risk Reduction	1/1/09	10/1/10
17	**NExScI**		
18	NExScI Sagan Fellowships	11/6/09 4/1/10	
19	NExSci Summer Workshop	7/20/09 7/19/10	
20	**Future Mission 1**		
21	Formulation	6/1/10	1/31/14
22	Baseline Reference Mission	7/1/11	
23	Issue Science AO	8/1/11	
24	Select Science Team	4/2/12	
25	Implementation	1/31/14	1/31/18
26			
27	**Program Governance**		
28	PCA	4/14/09	
29	Program Plan	9/1/09	
30	SRB ToR/Membership	9/1/09	
31	ExEP PIR	10/1/10 10/1/10
