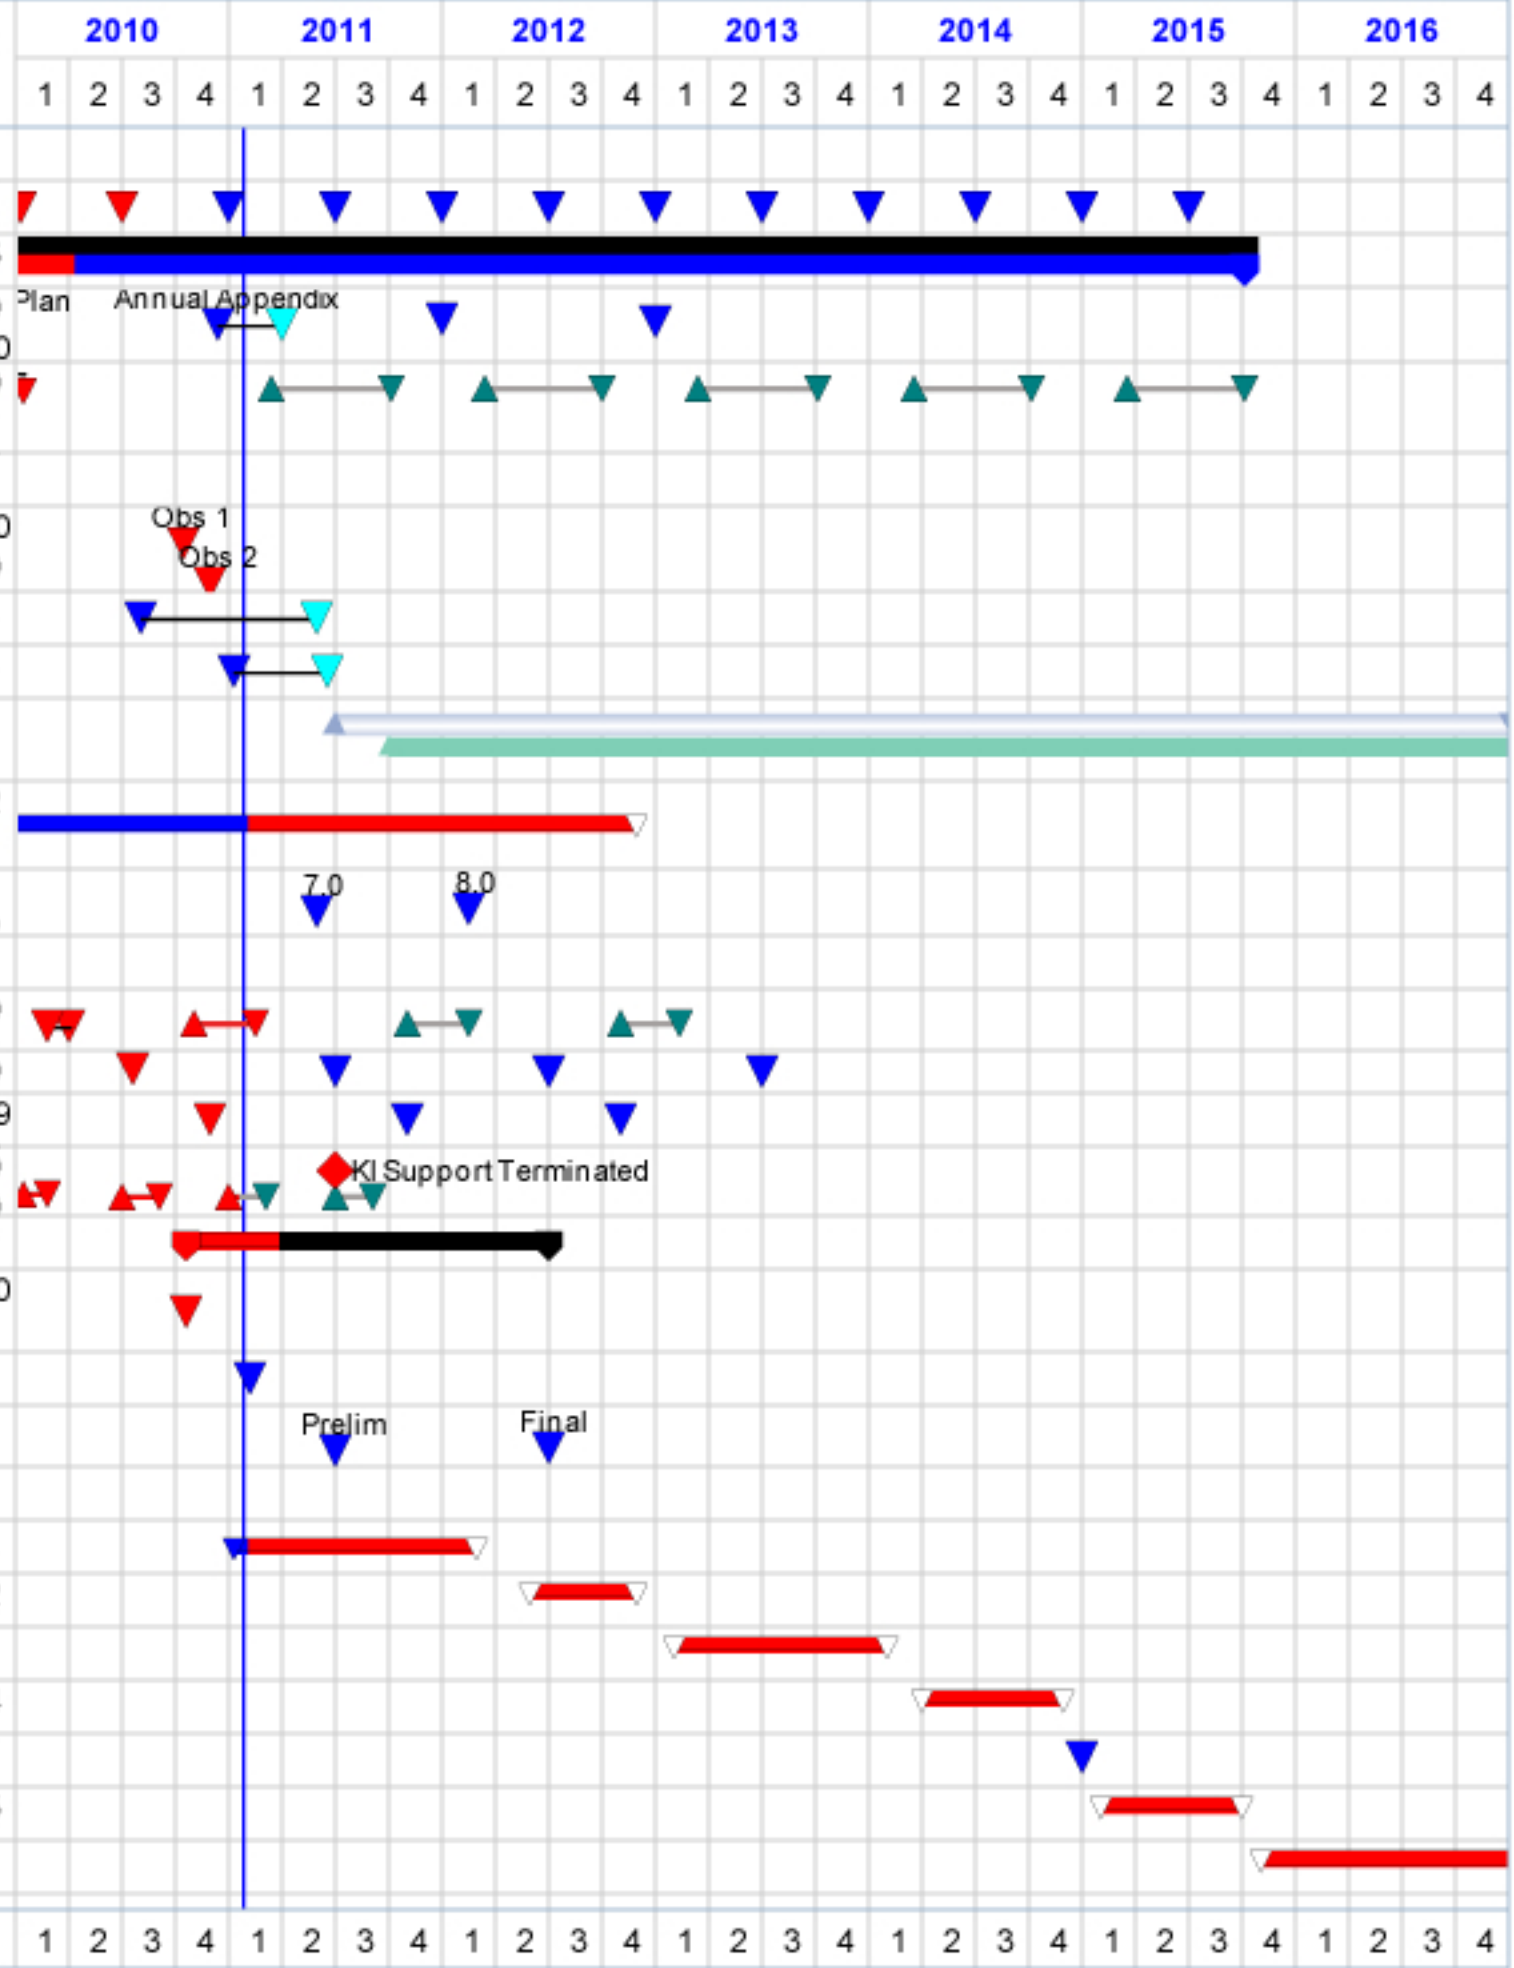Activity Name	Start Date	Finish Date
Program Planning		
ExoPAG Meetings	1/8/10	1/8/10
Exoplanet Technology	**6/1/09**	**10/6/15**
Technology Plan	6/16/09 12/15/10	6/16/09 12/15/10
Strategic Astrophysics Technology (call/select)	6/1/09 3/15/11	1/13/10 10/3/11
LBTI		
LBTI Reinstallation/Commissioning	10/16/10 12/1/10	10/16/10 12/1/10
AO Secondary #2	8/2/10	8/2/10
Shared Risk Science Start	1/10/11	1/10/11
LBTI NASA Operations	7/1/11	1/4/17
Kepler Science Operations	10/1/09	12/1/12
SOC Deliveries	6/1/11 2/15/12	6/1/11 2/15/12
NExScI		
NExScI Sagan Fellowships	11/5/09 4/1/10	11/5/09 4/1/10
Sagan Summer Workshops	7/20/09	7/20/09
Fellows Symposium	11/12/09	11/12/09
Keck Observing Calls/Proposals	6/15/09 1/15/10	8/19/09 2/22/10
WFIRST	**10/19/10**	**7/1/12**
Call for Science Definition Team	10/19/10	10/19/10
SDT first meeting	2/4/11	2/4/11
SDT Report	7/1/12 7/1/11	7/1/12 7/1/11
Future Mission: Exoplanet 1		
ExoPAG: Science Requirements/Scope	1/9/11	3/1/12
ISWG Call/Selection	6/1/12	12/1/12
Funded Concept Studies	2/1/13	2/1/14
NASA Senior Review Process	4/1/14	12/1/14
Baseline Reference Mission	1/1/15	1/1/15
DSIAC Review	2/1/15	10/1/15
Phase 2 Pre-formulation technology	11/1/15	6/1/19
